

City of Burlingame Proposed Community Center

City Council Study Session

September 17, 2018









AGENDA

- 1. Project Schedule Update
- 2. Project Overview and Updates
- 3. Council Action Requested:
 - Provide Input on:
 - Project Scope + Budget
 - Provide direction for Underground Parking
 - Approve CAC recommended Materials Palette
 - Approve Concept of Early Playground Site Package (Scope + Schedule)
- 4. Next Steps

PROJECT SCHEDULE: Community Center

	Schematic Design:	July – October 2018				
	 15% Construction Documents 	•				
	Refine Design and Select Building Systems					
	Develop Material and Color Palette					
	☐ Integrated Design Workshop (September)					
	☐ City Council Study Session (September) – TOI	DAY!				
	Planning Commission (September)					
	☐ Parks and Recreation Commission (September)					
	☐ Technical Meetings Round 2 - Planning, Building, Fire, Police (September)					
	☐ City Council Presentation (November 5)					
	 Design Development: 30% Construction Documents 	ember 2018- March 2019				
	Construction Documents:	April – September 2019				

Bid and Award:

Construction:

• 60%, 90% & Plan Check

September – December 2019

January 2020 - December 2021

BURLINGAME COMMUNITY CENTER PROJECT SCOPE





EARLY SITE PACKAGE – PLAYGROUND

- CIVIL
- LANDSCAPE
- ELECTRICAL



PROJECT SCHEDULES




PROJECT COST MODEL – Status

	Hard Cost	Soft Cost	Subtotal	Project Contingency	Escalation	Total		
PACKAGE 1: Early Site Package (Playground)								
Early Site Package Option	\$718,134	\$189,000	\$907,134	\$67,115	\$57,451	\$1,031,700		
PACKAGE 2: Building + Associate Site + Parking								
Option 1: 43 Underground								
parking spaces	\$31,289,341	\$9,012,000	\$40,301,341	\$2,924,239	\$3,588,239	\$46,813,819		
Option 2: 53 Underground								
parking spaces	\$32,208,119	\$9,254,000	\$41,462,119	\$2,993,457	\$3,691,693	\$48,147,269		
Community Center Building Project		¢7.520.000	¢22 012 017	¢0 200 711	¢0.057.157	\$20 E/0 E02		
(incl. FF&E & site work)		\$7,538,000	\$33,213,816	\$2,399,611	\$2,956,156	\$38,569,583		
Building FF&E	\$21,065,794	\$6,327,000	\$27,392,794	\$1,968,766	\$2,372,008	\$31,733,568		
	\$1,376,000	\$362,000	\$1,738,000	\$128,600	\$154,938	\$2,021,538		
Sitework	\$3,234,023	\$849,000	\$4,083,023	\$302,245	\$429,210	\$4,814,478		
Underground Parking								
43 spaces	\$5,613,525	\$1,474,000	\$7,087,525	\$524,629	\$632,083	\$8,244,236		
53 space	\$6,532,303	\$1,716,000	\$8,248,303	\$593,846	\$735,537	\$9,577,686		
ADD ALTERNIATES (incl. continuous in constation soft costs)								
ADD ALTERNATES (incl. contingencies, escalation, soft costs)						¢1 170 000		
Photovoltaic Panel System (on buildi	ng)					\$1,170,000		
Green Roof on Kid's Town						\$156,000		
Emergency Generator/ or Battery						\$310,000		
Elevator #2						\$340,000		



COUNCIL DIRECTION

UNDER BUILDING PARKING OPTION

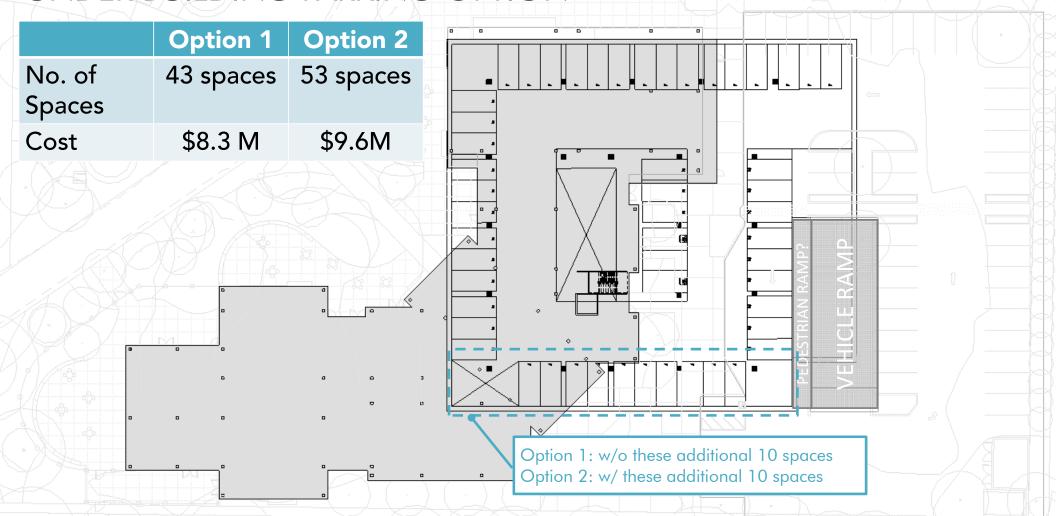

PROJECT COST MODEL – Add Alternates

Photovoltaic Panels

- Low Interest Loan from the State Energy Commission OR
- Power Purchase Agreement

Green Roof

Possible Fundraising Opportunity

Emergency Generator or Battery Back-Up

- Depending on costs maybe able to be funded through project contingency

• Elevator #2

- Depending on costs maybe able to be funded through project contingency



EXTERIOR PERSPECTIVES

BURLINGAME AVENUE ENTRY VIEW



EXTERIOR PERSPECTIVES

PARKSIDE VIEW



EXTERIOR PERSPECTIVES

WEST ELEVATION ON BURLINGAME AVENUE



BURLINGAME COMMUNITY CENTER


FLYTHROUGH ANIMATION











EXTERIOR ENVELOPE: EXTERIOR FINISHES





STUCCO





WOOD SOFFIT/TRELLISES








PAVILION METAL PANEL






STONE BASE



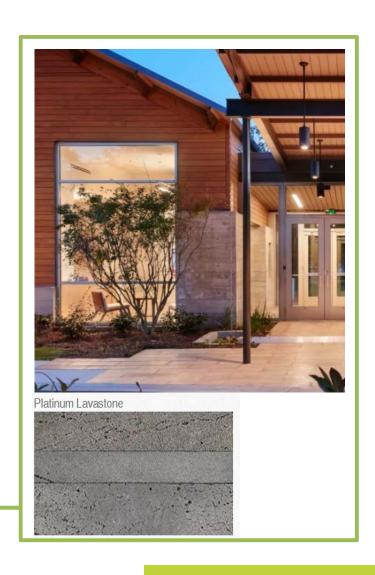

HORIZONTAL WOOD ACCENT

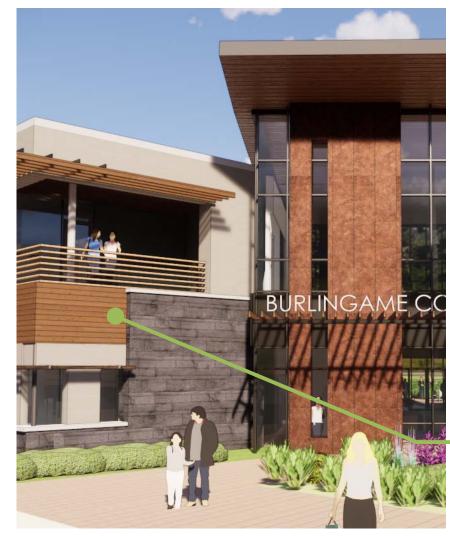



INPUT REQUESTED – Today

Council Input requested at tonight's Council Study Session:

- Provide input on the underground parking options.
- Approve scope and schedule for the early site package for the playground design and construction.
- Approve exterior material palette as recommended by the Advisory Committee.
- Provide input regarding preliminary exterior color palette.
- Provide input on the project scope and budget.

NEXT STEPS – 11/5 City Council Meeting

Council Action that will be requested at the November Council meeting:

- Direction and approval on the project budget.
- Approval of the schematic design package.





City of Burlingame Proposed Community Center

City Council Study Session

September 17, 2018







