


# 9/11 MEMORIAL

Warbird Park

# Progress To Date

- Site Selection – Warbird Park **Complete**
- Conceptual Layout of 9/11 Memorial **Complete**
- Contract with DDC for Site Prep Work & Landscape Design Services **Complete**
- Engage Low Country Monuments to Relocate Existing Structure **Complete**
- Verbal Authorization from Horry County Department of Airports **Complete**  
(will seek final approval upon completion of design)


# Monument Site Layout

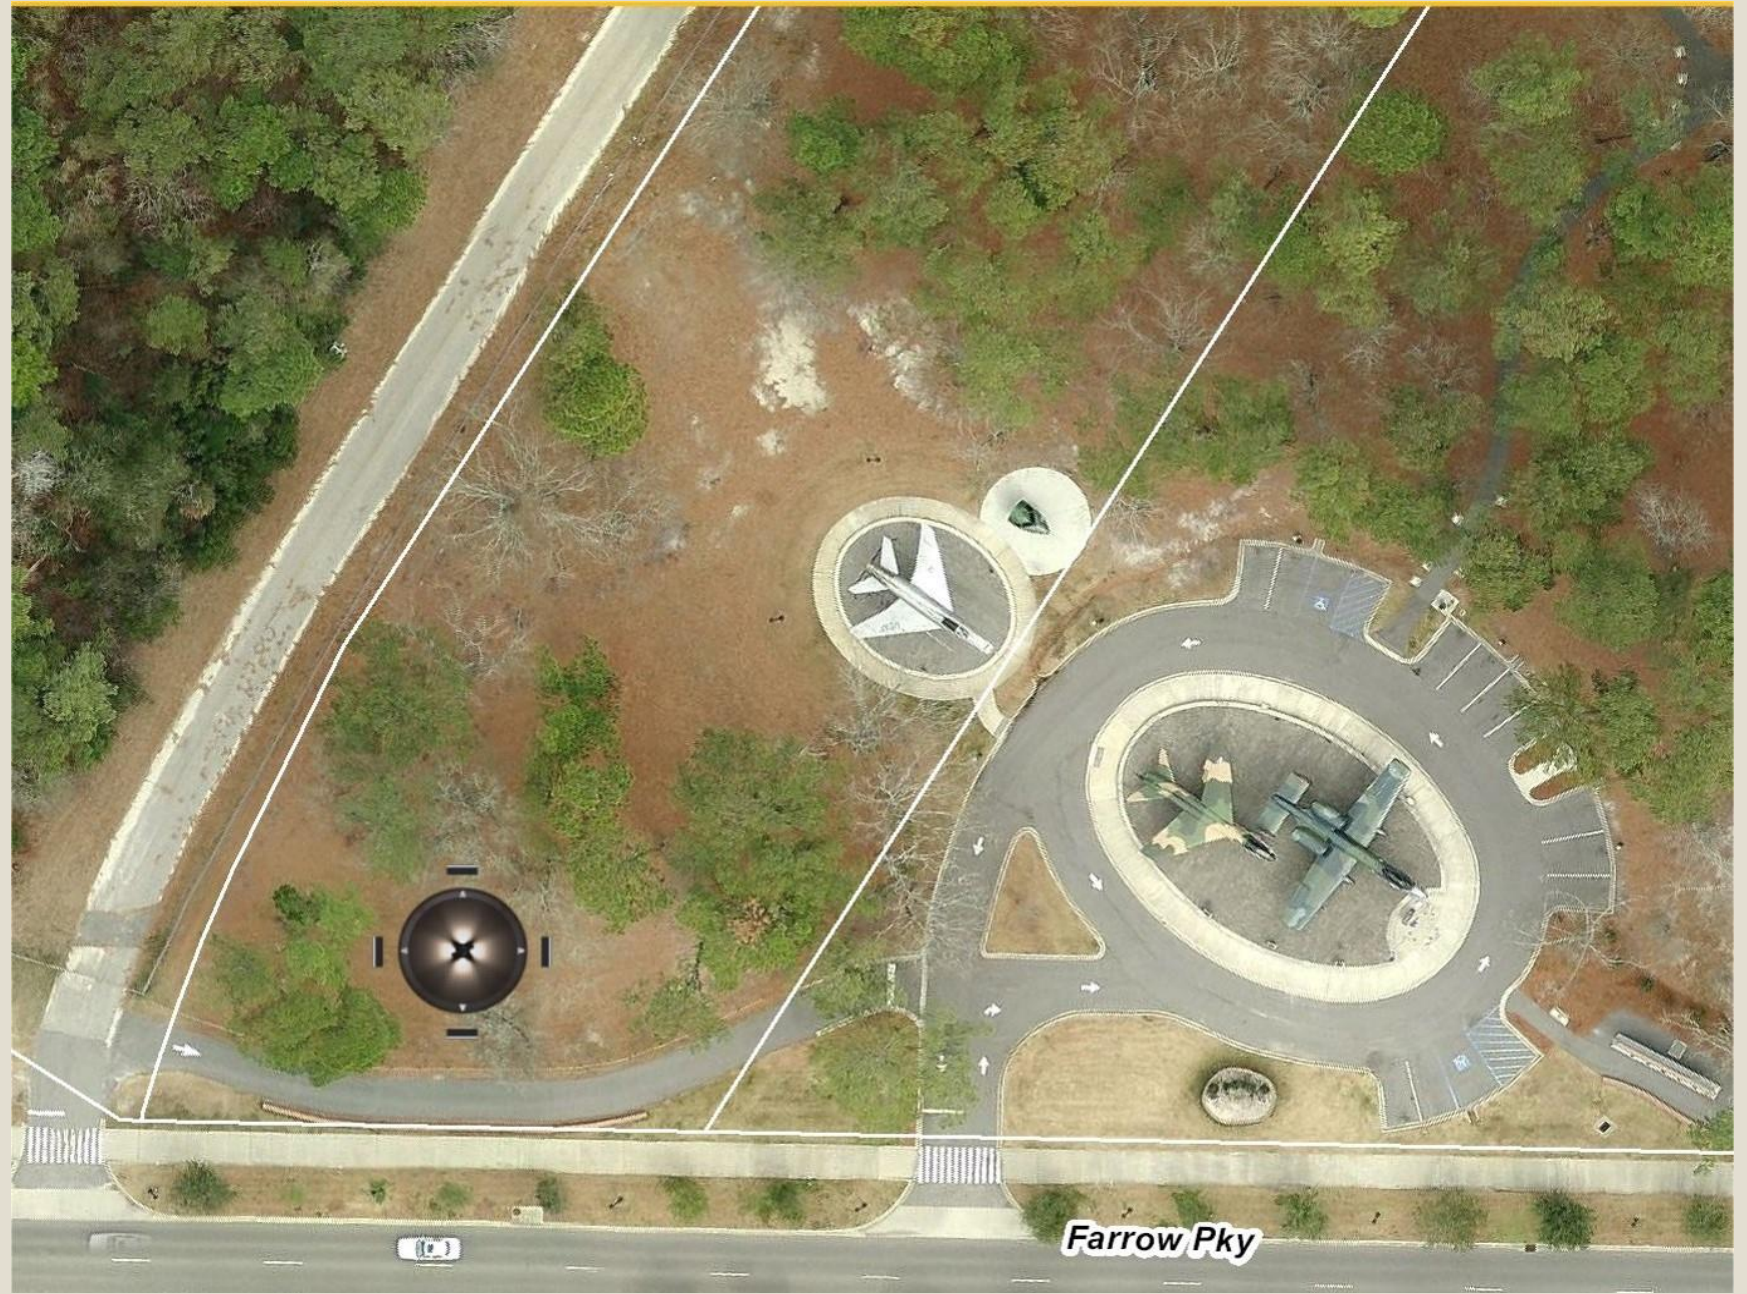



# Future Parking Area Layout

(As additional funds  
become available)

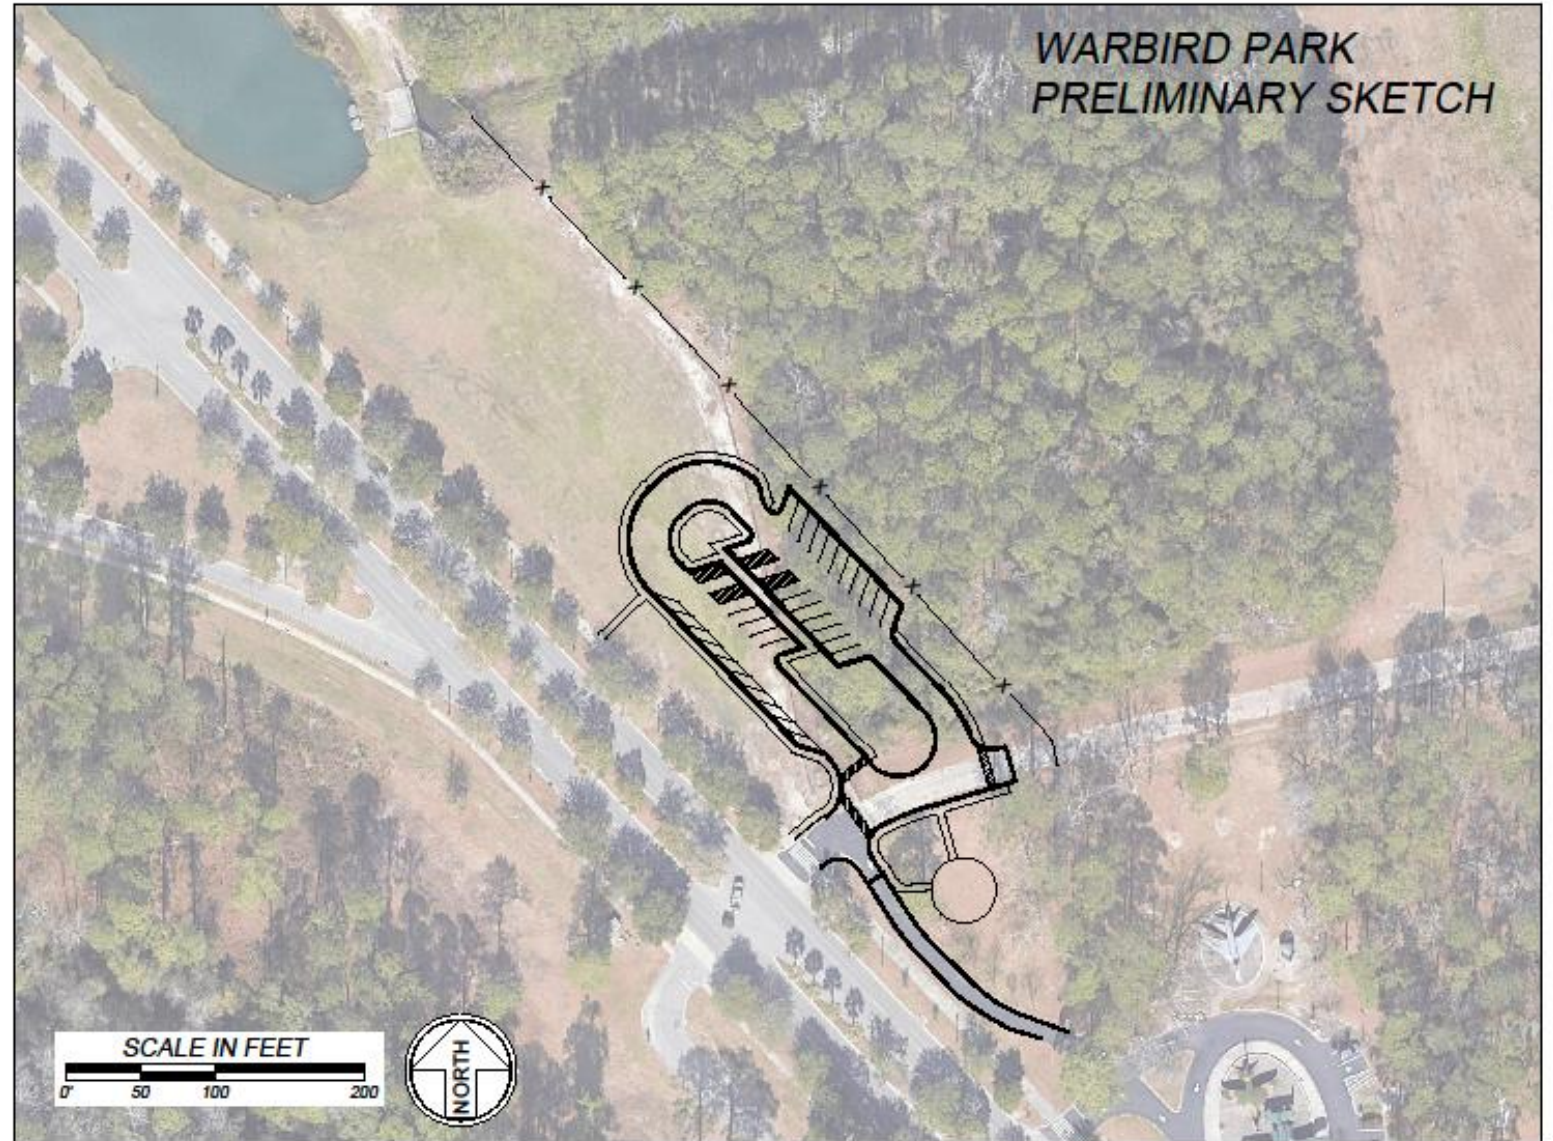



# Monument Rendering



# Next Steps

- Formal Authorization from City Council (February 2021)
- Finalize Monument and Landscape Design (In Progress)
- Obtain Final Cost Estimate to Relocate Monument (In Progress)
- Solicit bids for Site Work, Monument Pad, & Landscaping (May 2021)
- Monument Relocation (Scheduled for June 2021)
